Leadership Hermosa Beach Class of 2020

Project Timeline

ID	Task Name	Duration	Start	Finish
17	Submit Project to Brandy for Agenda	0 days	2/11/20	2/11/20
18	Brandy Prepares Agenda Item	14 days	2/11/20	2/25/20
15	Rain Barrel Fundraiser	0 days	2/15/20	2/15/20
1	City Council Meeting	0 days	2/25/20	2/25/20
5	Prepare Flagpole Permit Submittal	7 days	2/25/20	3/4/20
7	Brick Fundraising	35 days	2/26/20	4/3/20
14	Comedy and Magic Fundraiser	0 days	3/3/20	3/3/20
2	Flagpole Lead Time	42 days	3/4/20	4/17/20
6	Building Permit for Flagpole	28 days	3/4/20	4/2/20
16	St. Patrick's Day Parade	0 days	3/14/20	3/14/20
3	Flagpole Foundation	7 days	4/2/20	4/9/20
8	Brick Lead Time	21 days	4/3/20	4/26/20
4	Flagpole Installation	2 days	4/17/20	4/19/20
9	Preparation of Brick Area	6 days	4/19/20	4/26/20
13	Irrigation Installation (by Others)	7 days	4/19/20	4/27/20
10	Installation of Bricks	7 days	4/26/20	5/3/20
11	Landscape Completion (by Others)	6 days	5/3/20	5/9/20
12	Dedication Ceremony	0 days	5/9/20	5/9/20
19	Thank You Letters	7 days	5/9/20	5/17/20
20	Project Completion	0 days	5/17/20	5/17/20

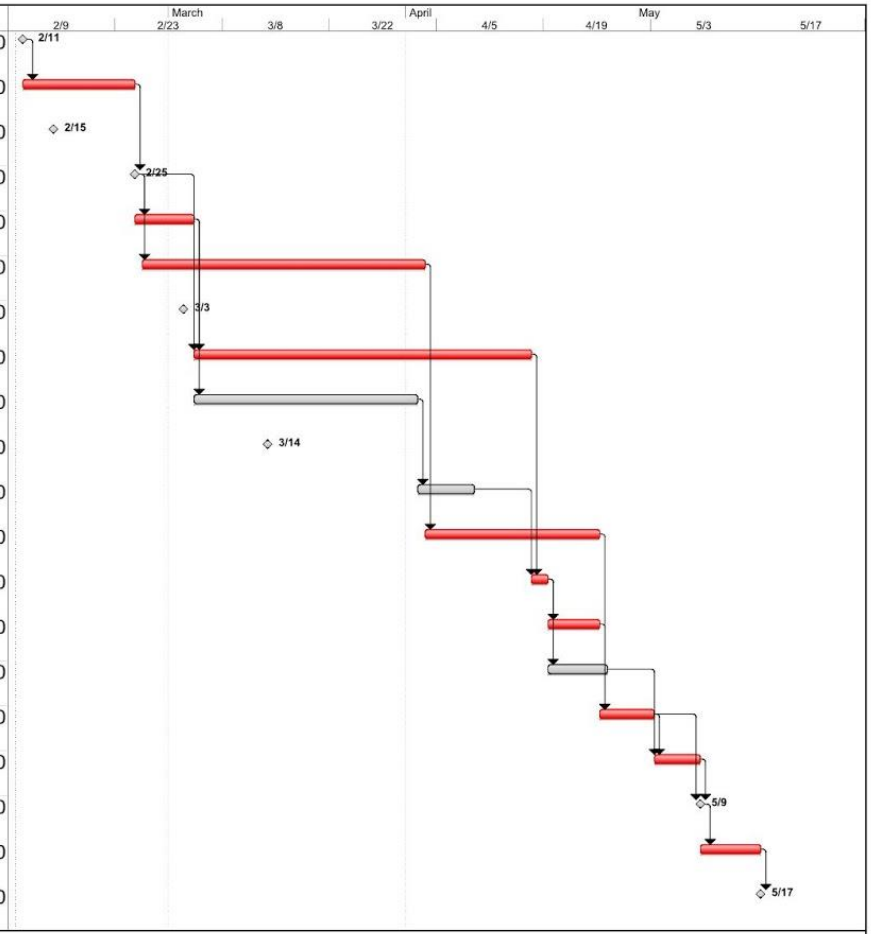

LEADERSHIP HERMOSA BEACH

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline | Critical Path
